ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	Create promotion material to solicit input	16 days	Tue 6/26/12	Tue 7/17/12		
2	Print promotional material	7 days	Wed 7/18/12	Thu 7/26/12	1	
3	Create Next100 web page	5 days	Wed 7/11/12	Tue 7/17/12		Jim
4	Ongoing maintenance of Next100 web page	90 days	Wed 7/18/12	Tue 11/20/12	3	
5	Distribute promotional material	25 days	Fri 7/27/12	Thu 8/30/12	2	
6	Draft press release	7 days	Fri 7/27/12	Mon 8/6/12		Raven
7	Prepare feedback form	7 days	Fri 7/27/12	Mon 8/6/12		Dan
8	Plan for community forum	25 days	Fri 7/27/12	Thu 8/30/12	2	
9	Property tour	1 day	Fri 8/31/12	Fri 8/31/12	5	
10	Radio spots	6 days	Thu 8/23/12	Thu 8/30/12		
11	First community forum	0 days	Fri 8/31/12	Fri 8/31/12	5,8,10,9	
12	plan for second community forum	30 days	Mon 9/3/12	Fri 10/12/12	11	
13	Second community forum	0 days	Fri 10/12/12	Fri 10/12/12	11FS+30 days,12	
14	Finalize the approach based on community input	14 days	Mon 10/15/12	Thu 11/1/12	13	
15	Prepare RFQ for architect	45 days	Fri 11/2/12	Thu 1/3/13	14	
16	Post RFQ	0 days	Thu 1/3/13	Thu 1/3/13	15	
17	RFQ in on the street	45 days	Fri 1/4/13	Thu 3/7/13	16	
18	Questions due	0 days	Wed 1/23/13	Wed 1/23/13	16FS+14 days	
19	answer questions	14 days	Thu 1/24/13	Tue 2/12/13	18	
20	Post answers	0 days	Tue 2/12/13	Tue 2/12/13	19	
21	Bids due	0 days	Thu 3/7/13	Thu 3/7/13	17	
22	Evaluate proposals	14 days	Fri 3/8/13	Wed 3/27/13	21	
23	Select finalists	0 days	Wed 3/27/13	Wed 3/27/13	22	
24	Interviews	7 days	Thu 3/28/13	Fri 4/5/13	23	
25	Select architect	7 days	Mon 4/8/13	Tue 4/16/13	24	
26	Award contract to architect	0 days	Tue 4/16/13	Tue 4/16/13	25	
27	Meetings with Architect	21 days	Tue 5/7/13	Tue 6/4/13	26FS+14 days	
28	Architect creates plan	60 days	Wed 6/5/13	Tue 8/27/13	27	
29	Prepare bond documents	30 days	Wed 8/28/13	Tue 10/8/13	28	
30	Post bond vote notice	0 days	Mon 9/16/13	Mon 9/16/13	28FS+14 days	
31	Bond vote	0 days	Mon 11/4/13	Mon 11/4/13		

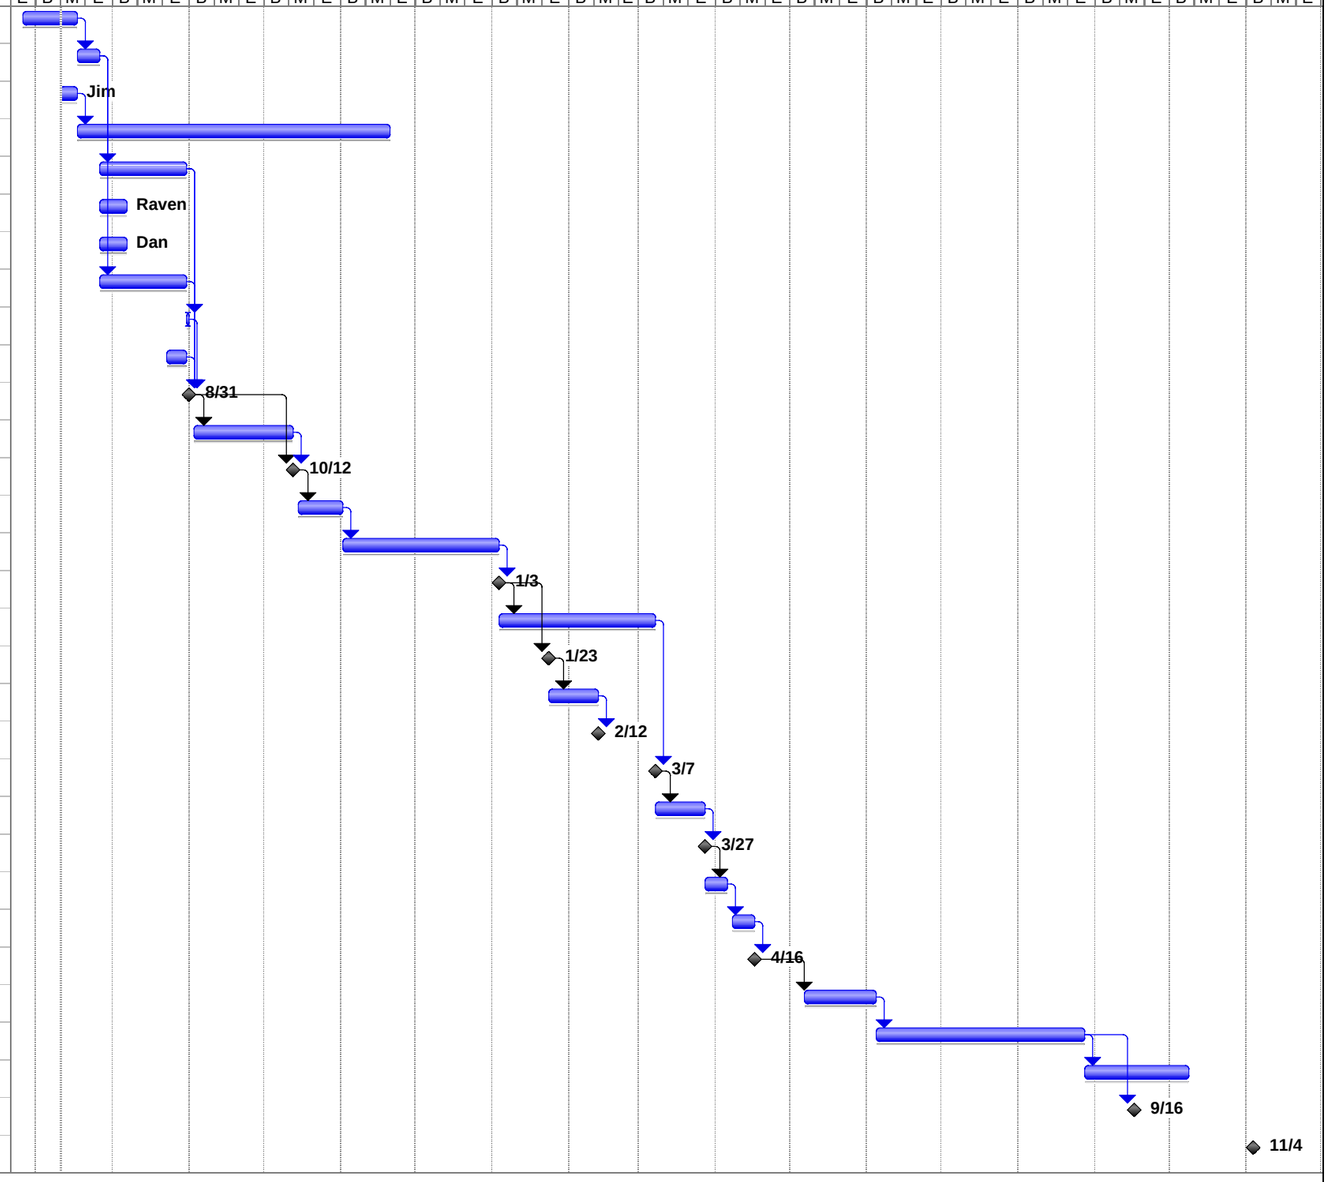

Project: HighLevelProjectPlan.mpp
Date: Wed 7/11/12

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
